


Creekside District Master Plan Timeline

Project Activity	2012					2013					2014					2015										
	Apr.	May	Jun.	Jul.	Aug.	Sept.	Oct.	Nov.	Dec.	Jan.	Feb.	Mar.	Apr.	May	Jun.	Jul.	Aug.	Sept.	Oct.	Nov.	Dec.	Jan.	Feb.	Mar.	Apr.	
0.0 Meetings, Briefings and Outreach																										
CC/PC Council / Planning Commission				CC			PC/CC																			
SC Project Steering Committee																										
CH Stakeholder Charrettes						CH		CH	CH																	
OH/FG Open House / Focus Groups																										
OH										OH	OH								OH							
FG												FG														
1.1 Administration & Implementation																										
Task: 1 Workplan & eLogic Model Final																										
Task: 2 Biannual Reporting																										
Task: 3 Annual Logic Model Reporting																										
Task: 4 Final Project Report																										
Task: 5 City Budget & CIP Prep																										
Task: 6 Annual Funding Assessment																										
1.2: Project Identity, Steering Committee Formation and Guiding Principles																										
Task: 1 Create Creekside District project identity, website & communication materials																										
Task: 2 Draft and release RFPs																										
Task: 3 Select Consultant																										
Task: 4 Create Communications & Outreach Strategy				CC																						
Task: 5 Form Creekside District Steering Committee																										
Task: 6 Develop guiding principles for Creekside District project																										
1.3: Baseline Assessment																										
Task: 1 Establish geographies for study																										
Task: 2 Compile and synthesize data																										
Task: 3 Prepare indicators brochure template & baseline data																										
Task: 4 Conduct PhotoVoice community input program & present results																										
Task: 5 Publish indicators brochure																										
2.1 Downtown Creeks Natural Resource Plan																										
Task: 1 Kickoff Meeting																										
Task: 2 Stakeholder and property owner engagement																										
Task: 3 Sub-basin conditions assessment of creeks and creek-adjacent properties																										
Task: 4 Establish compliance requirements																										
Task: 5 Initial solutions package (performance standards, design options, regulatory program)																										
Task: 6 Pilot project #1 design and engineering																										
Task: 7 Refinement of solutions package																										
Task: 8 Pilot project #2 design and engineering																										
Task: 9 Draft projects and programs package																										
Task: 10 Stakeholder and agency selection of preferred projects and programs																										
Task: 11 Draft recommendation on code & amendments																										
Task: 12 Natural Resource Plan Public Draft																										
Task: 13 Natural Resource Plan Adoption																										
Task: 14 Draft amendments to Comprehensive Plan, development code & manuals & IGAs																										
Task: 15 IGAs, MOUs, code and amendments adoption																										
2.2: Canyon Road Streetscape Enhancement & District Transportation Plan																										
Task: 1 Kickoff Meeting																										
Task: 2 Conduct Mobility Audit of Creekside District & Canyon Road																										
Task: 3 Mobility Audit report and recommendations																										
Task: 4 Recommend to City Council adoption of Complete Streets policy & CSS directive																										
Task: 5 Conduct working session on Canyon Road design (City, State, Regional agencies)																										
Task: 6 Create memorandum of understanding and exhibits for Canyon Road design																										
Task: 7 Evaluate Canyon Rd Special Transportation Area designation																										
Task: 8 Outreach to area businesses, property owners, and other stakeholders																										
Task: 9 Draft access management & implementation strategy for Canyon Road																										
Task: 10 Initial transportation solutions package for Creekside District, including MMA criteria																										
Task: 11 Transportation modeling																										
Task: 12 CSS Pilot projects #1 & 2 Crescent Street Connection & Dawson Way																										
Task: 13 Refinement and selection of solutions																										
Task: 14 Draft amendments to Comprehensive Plan, development code & manuals & IGAs																										
Task: 15 IGAs, MOUs, code and amendments adoption																										
Task: 16 Complete preliminary engineering Canyon Road (up to 10%)																										

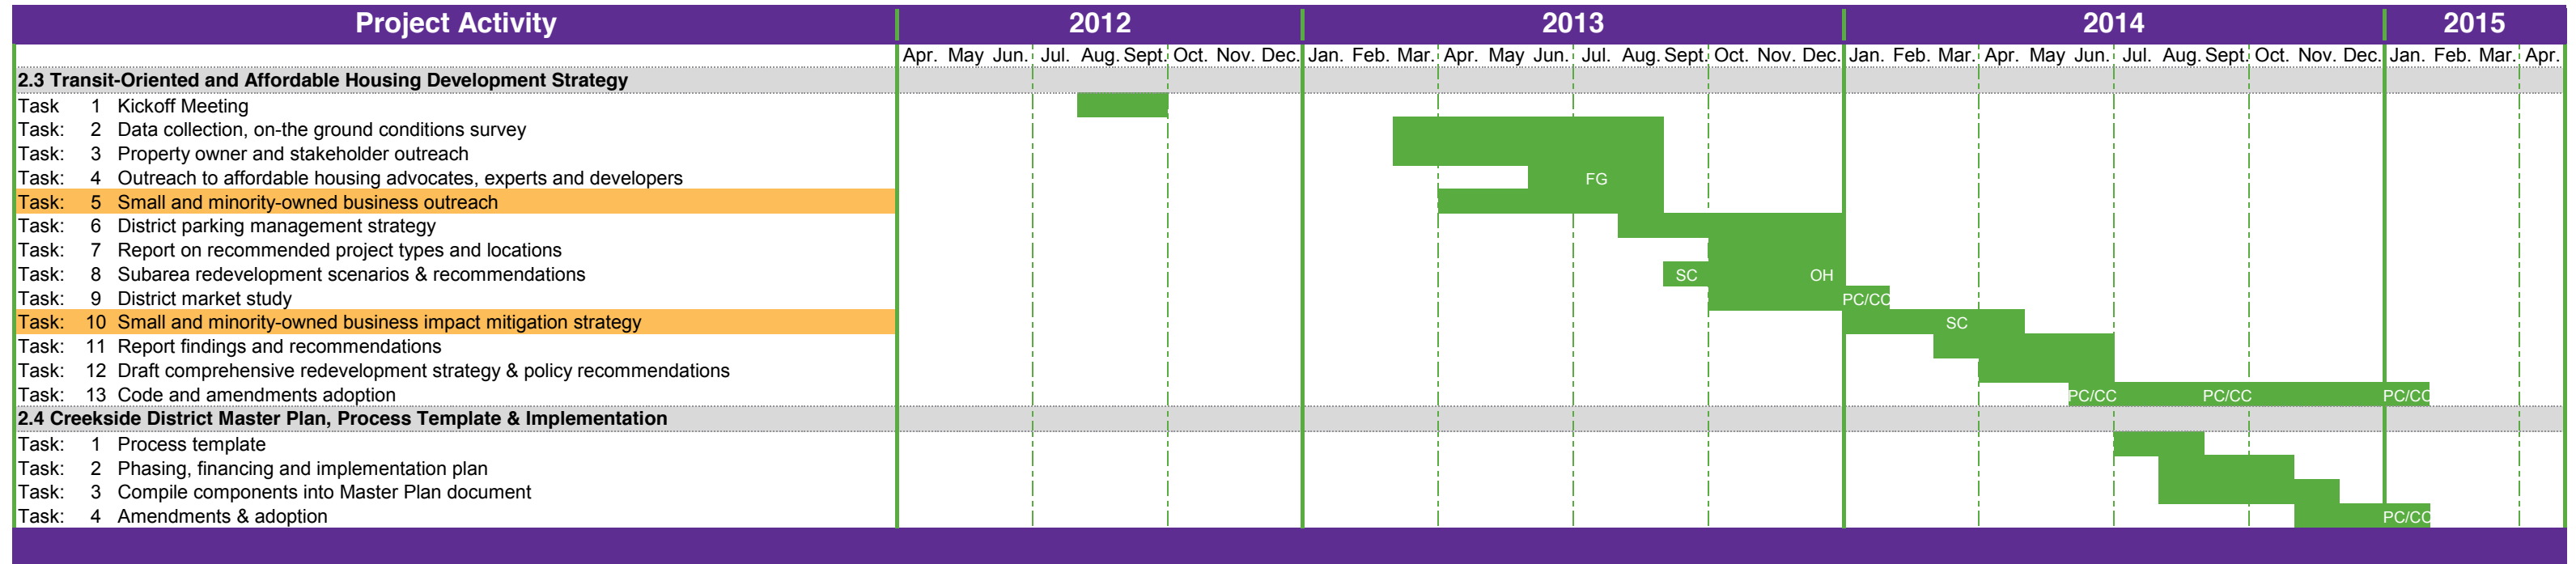

 Outreach to populations traditionally underrepresented in planning
